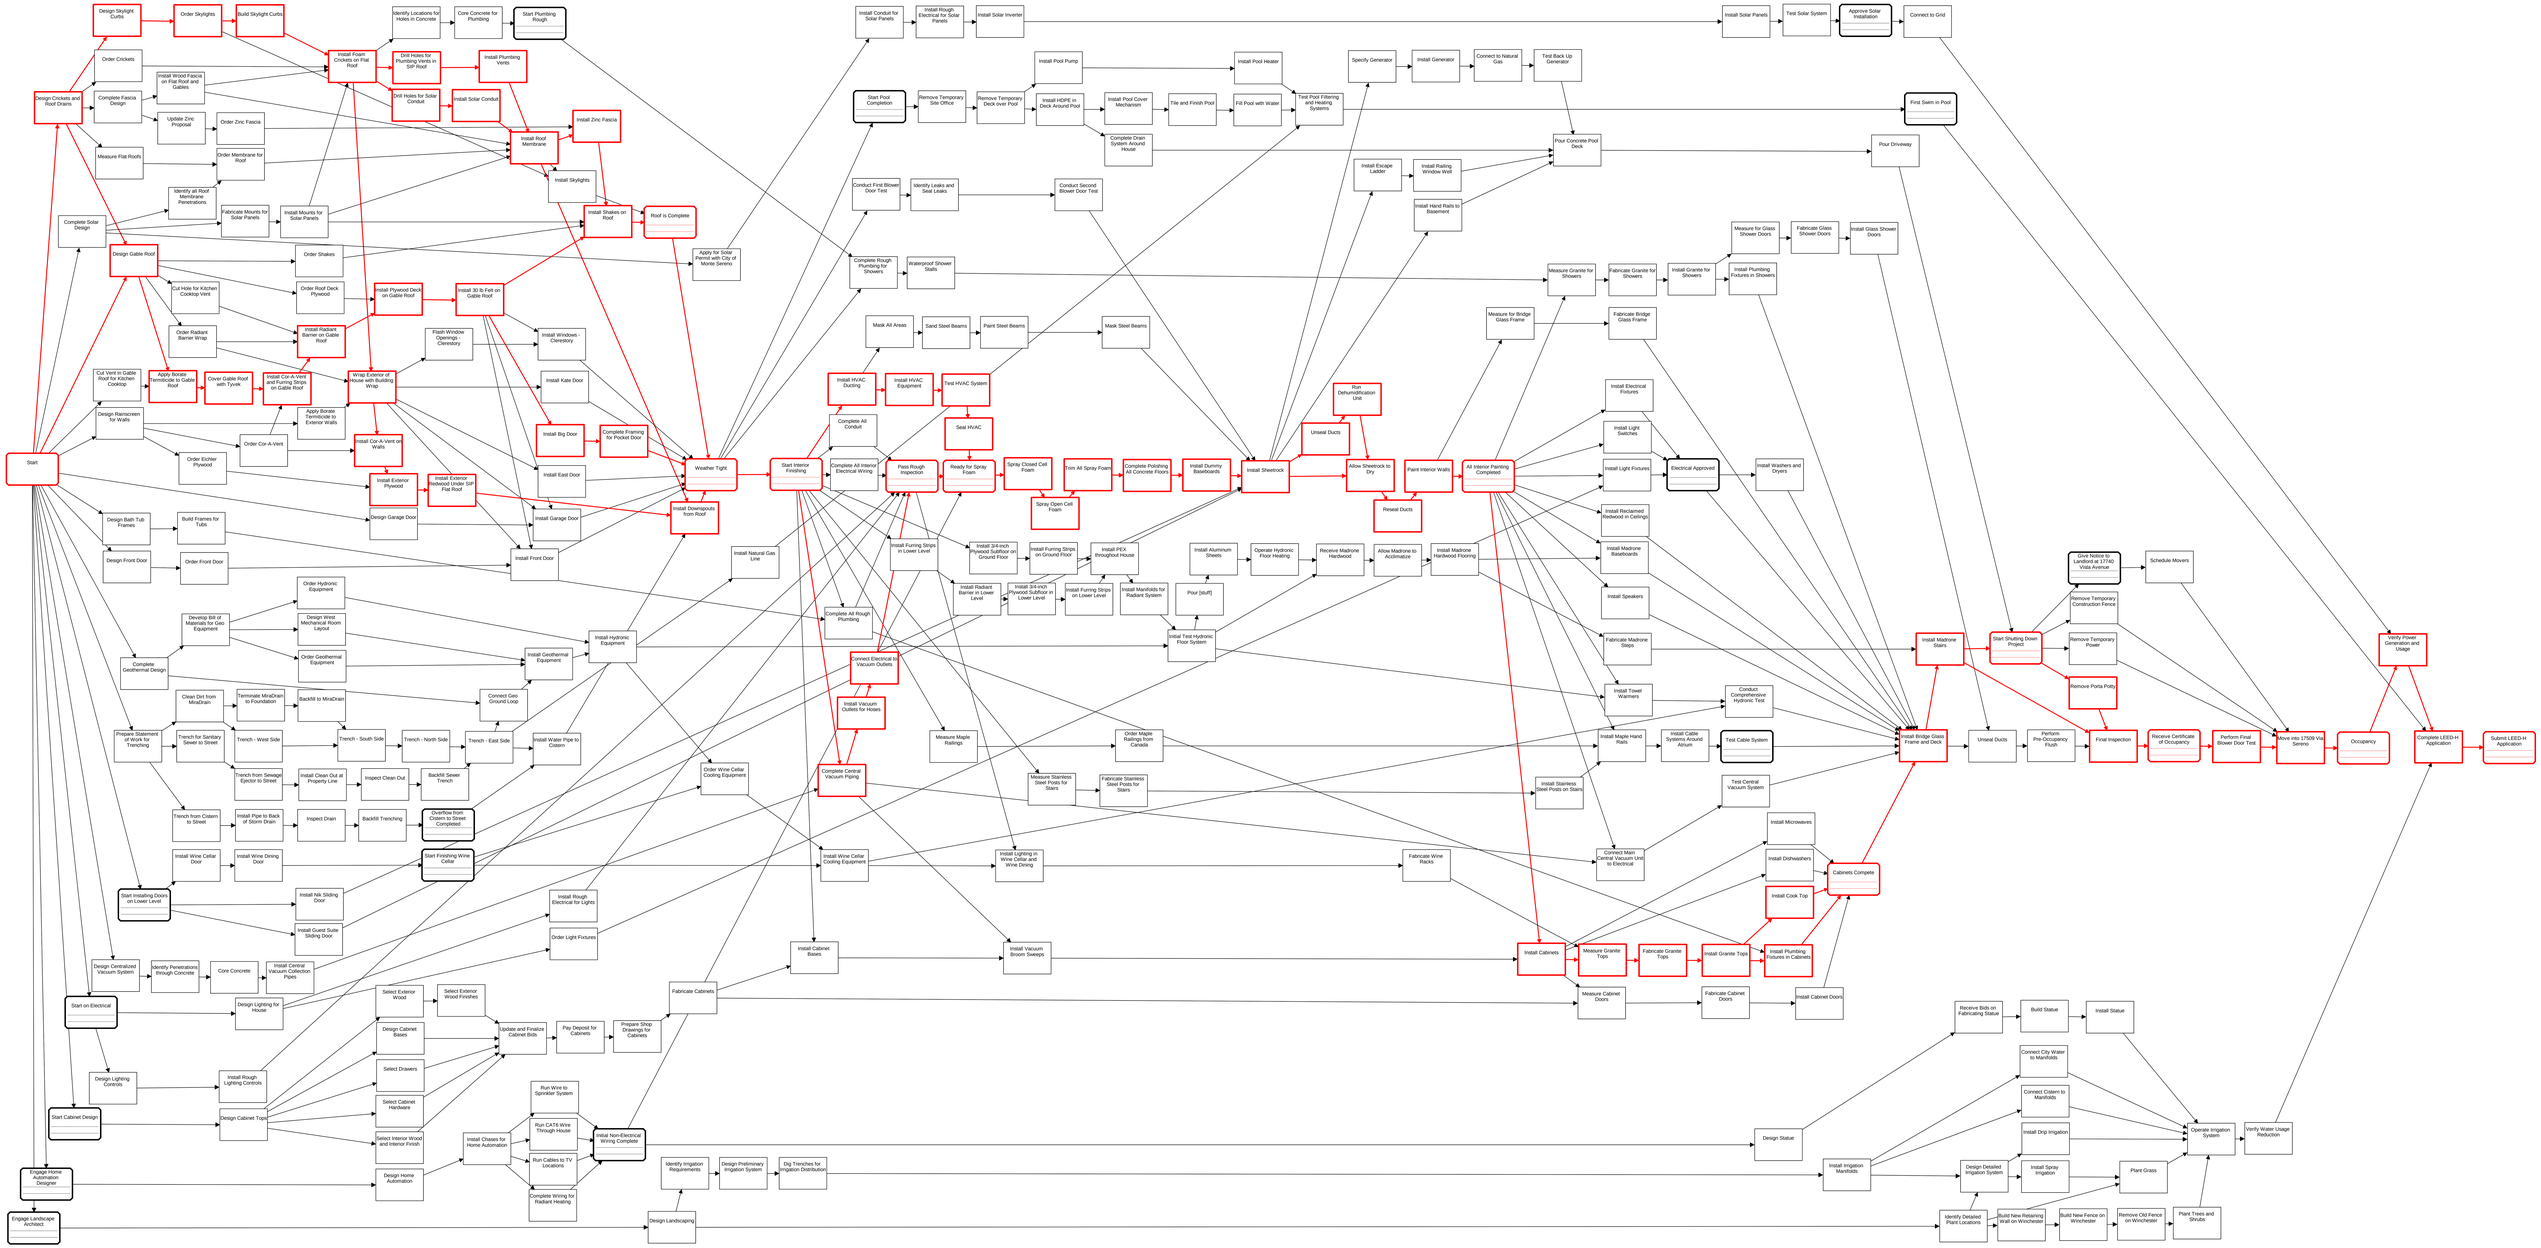
Start
Design Skylight Curbs
Order Skylights
Build Skylight Curbs
Order Crickets
Design Crickets and Roof Drains
Complete Fascia Design
Install Wrtod Fascia on Flat Roof and Gables
Update Zinc Proposal
Order Zinc Fascia
Measure Flat Roofs
Order Membrane for Roof
Identify all Roof Membrane Penetrations
Fabricate Mounts for Solar Panels
Install Mounts for Solar Panels
Complete Solar Design
Design Gable Roof
Order Shakes
Cut Hole for Kitchen Cooktop Vent
Order Roof Deck Plywood
Install Plywood Deck on Gable Roof
Install 30 lb Felt on Gable Roof
Order Radiant Barrier Wrap
Install Radiant Barrier on Gable Roof
Cut Vent in Gable Roof for Kitchen Cooktop
Apply Borate Termitocide to Gable Roof
Cover Gable Roof with Tyvek
Install Cor-A-Vent and Furring Strips on Gable Roof
Wrap Exterior of House with Building Wrap
Design Rainscreen for Walls
Apply Borate Termitocide to Exterior Walls
Order Cor-A-Vent
Install Cor-A-Vent on Walls
Order Eichler Plywood
Install Exterior Plywood
Install Exterior Redwood Under SIP Flat Roof
Design Garage Door
Install Garage Door
Design Bath Tub Frames
Build Frames for Tubs
Design Front Door
Order Front Door
Install Front Door
Develop Bill of Materials for Geo Equipment
Order Hydronic Equipment
Design Wrest Mechanical Room Layout
Order Geothermal Equipment
Complete Geothermal Design
Install Geothermal Equipment
Install Hydronic Equipment
Clean Dirt from MiraDrain
Terminate MiraDrain to Foundation
Backfill to MiraDrain
Connect Geo Ground Loop
Prepare Statement of Work for Trenching
Trench for Sanitary Sewer to Street
Trench - West Side
Trench - South Side
Trench - North Side
Trench - East Side
Install Water Pipe to Cistern
Trench from Sewage Ejector to Street
Install Clean Out at Property Line
Inspect Clean Out
Backfill Sewer Trench
Trench from Cistern to Street
Install Pipe to Back of Storm Drain
Inspect Drain
Backfill Trenching
Overflow from Cistern to Street - Completed
Install Wine Cellar Door
Install Wine Dining Door
Start Finishing Wine Cellar
Start Installing Doors on Lower Level
Install Nik Sliding Door
Install Guest Suite Sliding Door
Design Centralized Vacuum System
Identify Penetrations through Concrete
Core Concrete
Install Central Vacuum Collection Pipes
Start on Electrical
Design Lighting for House
Design Lighting Controls
Install Rough Lighting Controls
Start Cabinet Design
Design Cabinet Tops
Engage Home Automation Designer
Engage Landscape Architect
Install Roof Membrane
Install Skylights
Install Shakes on Roof
Roof is Complete
Apply for Solar Permit with City of Monte Sereno
Weather Tight
Install Downspouts from Roof
Identify Locations for Holes in Concrete
Core Concrete for Plumbing
Start Plumbing Rough
Install Foam Crickets on Flat Roof
Drill Holes for Plumbing Vents in SIP Roof
Install Plumbing Vents
Drill Holes for Solar Conduit
Install Solar Conduit
Install Zinc Fascia
Install Windows - Clerestory
Flash Window Openings - Clerestory
Install Kate Door
Install Big Door
Complete Framing for Pocket Door
Install East Door
Install Natural Gas Line
Install Vacuum Outlets for Hoses
Connect Electrical to Vacuum Outlets
Complete Central Vacuum Piping
Order Wine Cellar Cooling Equipment
Install Wine Cellar Cooling Equipment
Install Rough Electrical for Lights
Order Light Fixtures
Install Cabinet Bases
Fabricate Cabinets
Select Exterior Wood
Select Exterior Wood Finishes
Design Cabinet Bases
Select Drawers
Select Cabinet Hardware
Select Interior Wood and Interior Finish
Design Home Automation
Update and Finalize Cabinet Bids
Pay Deposit for Cabinets
Prepare Shop Drawings for Cabinets
Install Chases for Home Automation
Run Wire to Sprinkler System
Run CAT6 Wire Through House
Run Cables to TV Locations
Complete Wiring for Radiant Heating
Intial Non-Electrical Wiring Complete
Identify Irrigation Requirements
Design Preliminary Irrigation System
Dig Trenches for Irrigation Distribution
Design Landscaping
Install Conduit for Solar Panels
Install Rough Electrical for Solar Panels
Install Solar Inverter
Install Solar Panels
Test Solar System
Approve Solar Installation
Connect to Grid
Install Pool Pump
Install Pool Heater
Specify Generator
Install Generator
Connect to Natural Gas
Test Back Up Generator
Start Pool Completion
Remove Temporary Site Office
Remove Temporary Deck over Pool
Install HDPE in Deck Around Pool
Install Pool Cover Mechanism
Tile and Finish Pool
Fill Pool with Water
Test Pool Filtering and Heating Systems
Complete Drain System Around House
Pour Concrete Pool Deck
Pour Driveway
First Swim in Pool
Install Escape Ladder
Install Railing Window Wall
Install Hand Rails to Basement
Conduct First Blower Door Test
Identify Leaks and Seal Leaks
Conduct Second Blower Door Test
Complete Rough Plumbing for Showers
Waterproof Shower Stalls
Measure Granite for Showers
Fabricate Granite for Showers
Install Granite for Showers
Measure for Glass Shower Doors
Fabricate Glass Shower Doors
Install Glass Shower Doors
Install Plumbing Fixtures in Showers
Mask All Areas
Sand Steel Beams
Paint Steel Beams
Mask Steel Beams
Measure for Bridge Glass Frame
Fabricate Bridge Glass Frame
Install HVAC Ducting
Install HVAC Equipment
Test HVAC System
Seal HVAC
Complete All Conduit
Run Dehumidification Unit
Unseal Ducts
Install Electrical Fixtures
Install Light Switches
Install Light Fixtures
Electrical Approved
Install Washers and Dryers
Start Interior Finishing
Complete All Interior Electrical Wiring
Pass Rough Inspection
Ready for Spray Foam
Spray Closed Cell Foam
Spray Open Cell Foam
Trim All Spray Foam
Complete Polishing All Concrete Floors
Install Dummy Baseboards
Install Sheetrock
Allow Sheetrock to Dry
Reseal Ducts
Paint Interior Walls
All Interior Painting Completed
Install Reclaimed Redwood in Ceilings
Install Madrone Baseboards
Install Speakers
Fabricate Madrone Steps
Install Towel Warmers
Install Maple Hand Rails
Install Cable Systems Around Atrium
Test Cable System
Install Madrone Stairs
Start Shutting Down Project
Give Notice to Landlord at 17740 Vista Avenue
Schedule Movers
Remove Temporary Construction Fence
Remove Temporary Power
Remove Porta Potty
Install Bridge Glass Frame and Deck
Unseal Ducts
Perform Pre-Occupancy Flush
Final Inspection
Receive Certificate of Occupancy
Perform Final Blower Door Test
Move into 17509 Via Sereno
Occupancy
Verify Power Generation and Usage
Complete LEED-H Application
Submit LEED-H Application
Install Natural Gas Line
Complete All Rough Plumbing
Install Furring Strips in Lower Level
Install 3/4-inch Plywood Subfloor on Ground Floor
Install Furring Strips on Ground Floor
Install PEX throughout House
Install Radiant Barrier in Lower Level
Install 3/4-inch Plywood Subfloor in Lower Level
Install Furring Strips on Lower Level
Install Manifolds for Radiant System
Pour [stuff]
Install Test Hydronic Floor System
Install Aluminum Sheets
Operate Hydronic Floor Heating
Receive Madrone Hardwood
Allow Madrone to Acclimatize
Install Madrone Hardwood Flooring
Measure Maple Railings
Order Maple Railings from Canada
Measure Stainless Steel Posts for Stairs
Fabricate Stainless Steel Posts for Stairs
Install Stainless Steel Posts on Stairs
Test Central Vacuum System
Connect Main Central Vacuum Unit to Electrical
Conduct Comprehensive Hydronic Test
Install Lighting in Wine Cellar and Wine Dining
Fabricate Wine Racks
Install Vacuum Broom Sweeps
Install Cabinets
Measure Granite Tops
Fabricate Granite Tops
Install Granite Tops
Install Plumbing Fixtures in Cabinets
Install Microwaves
Install Dishwashers
Install Cook Top
Cabinets Complete
Measure Cabinet Doors
Fabricate Cabinet Doors
Install Cabinet Doors
Receive Bids on Fabricating Statue
Build Statue
Install Statue
Design Statue
Connect City Water to Manifolds
Connect Cistern to Manifolds
Install Drip Irrigation
Install Irrigation Manifolds
Design Detailed Irrigation System
Install Spray Irrigation
Operate Irrigation System
Verify Water Usage Reduction
Plant Grass
Identify Detailed Plant Locations
Build New Retaining Wall on Winchester
Build New Fence on Winchester
Remove Old Fence on Winchester
Plant Trees and Shrubs
